

Team Monsrow

[*Engineering Solutions for Real-World Problems*]

BUSINESS PROPOSAL

VENUS - SCHOOL MANAGEMENT SYSTEM

[A Custom-Built, Modular Platform for Complete School Operations]

PREPARED BY

Vishal M & Team Monsrow

ISSUE DATE

25 July 2026

PROPOSAL VALID UNTIL

04 August 2026

Table of Contents

1. Executive Summary	3
2. Understanding Your Requirements	3
3. Proposed Solution Overview	3
4. Scope of Work	4
5. Technical Approach	6
6. Key Benefits & Value Proposition	7
7. Implementation Timeline & Milestones	7
8. Investment & Commercial Proposal	8
9. Payment Schedule	8
10. Post-Launch Support & Maintenance	8
11. Terms & Conditions	9
12. Assumptions & Exclusions	9
13. Why Partner With Team Monsrow	9
14. Next Steps	10
15. Contact & Signature Block	10

1. Executive Summary

Team Monsrow is pleased to present this proposal to Venus School for the design, development, and deployment of a comprehensive, custom-built School Management System. The platform will unify student records, staff administration, academics, communication, and finance into a single, secure, real-time system — replacing manual, disconnected processes with transparency, accountability, and data-driven decision-making at every level of the institution's operations.

Built on a modern, scalable technology stack and backed by dedicated infrastructure, the proposed system is designed to serve Venus School's day-to-day needs today while comfortably supporting the school's growth in the years ahead.

2. Understanding Your Requirements

Through our discussions with Venus School, we understand that the institution currently manages its academic and administrative operations largely through a manual, paper-based approach. This has created several operational challenges that the proposed system has been scoped specifically to resolve:

- Limited transparency — student, staff, academic and financial data is scattered across manual registers and disconnected files, making it difficult for stakeholders to access consistent, up-to-date information.
- Communication gaps with parents — there is no structured or reliable channel through which the school can share timely updates on attendance, fees, academics or events, weakening parent engagement.
- Difficulty in decision-making — without a centralized dashboard or consolidated reporting, school leadership lacks real-time visibility into key metrics, which slows down informed, timely decisions.

3. Proposed Solution Overview

To address these challenges, Monsrow proposes the Venus School Management System (VSMS) — a modular, secure, web-based platform purpose-built to bring every core school operation onto one connected system.

VSMS replaces fragmented manual processes with structured digital workflows, gives school leadership real-time visibility through dashboards and custom reports, opens a direct and reliable communication channel with parents via SMS, and enforces role-based access so that every user — from Super Admin to teaching staff — sees only what is relevant to their role. The system is delivered across eleven integrated modules, detailed in the following section.

4. Scope of Work

1. User Roles & Access Control Management

This foundational module dictates security and data governance across the entire application, utilizing a strict three-tier hierarchy.

- **Super Admin Control:** Full, unrestricted access to all modules, settings, and data.
- **Role Creation & Delegation:** The Super Admin can create 'Admin' and 'Staff' accounts.
- **Granular Permissions:** Super Admin can allocate specific read, write, update, and delete (CRUD) permissions to Admins and Staff on a per-module basis.
- **Centralized Security:** Ensures lower roles only interact with data and features strictly necessary for their daily tasks.

2. Class & Subject Management

A comprehensive module to structure the academic framework of the school.

- **Class Creation:** Setup and manage classes, sections, and batches (controlled by Super Admin; delegable to Admin/Staff).
- **Subject Repository:** Create, update, and manage a master list of all academic subjects.
- **Resource Allocation:** Map specific subjects to specific classes.

3. Student Lifecycle Management

Complete oversight of student data from admission to graduation.

- **CRUD Operations:** Full capability to create, read, update, and delete student records based on role permissions.
- **Automated Utilities:** System-generated student IDs and automated student mapping.
- **Document Management:** Secure, centralized digital storage for student documents and certificates.
- **Quick Access:** Advanced search filters and the ability to maintain "starred" or favorite student lists for rapid retrieval.

4. Staff & Personnel Management

A centralized human resources module acting as the single source of truth for all school employees.

- **Comprehensive Profiles:** Detailed records including qualifications, contact information, and employment history.
- **Role Mapping:** Clear visibility into which classes and subjects are assigned to each staff member.
- **Workload Tracking:** Administrative oversight of teacher schedules and assigned duties.
- **Access-Controlled Updates:** Staff data CRUD operations governed strictly by Super Admin permissions.

5. Academic Year Management

Purpose-built tools to handle the lifecycle of the school calendar and historical data.

- **Session Initialization:** Dedicated tools to create and configure new academic years.
- **Promotion Workflows:** Automated, guided processes for year-end student promotions and graduations.
- **Data Archiving:** Securely archive historical data from previous years without losing access for future reference or audits.

6. Marks & Examination Management

An end-to-end digital grading and evaluation ecosystem.

- **Custom Exam Setup:** Ability to define exam types, terms, and configurable grading rubrics.
- **Automated Output:** System-generated report cards ready for digital sharing or printing.
- **Performance Analytics:** Dashboards detailing class performance, subject averages, and pass/fail ratios.
- **Audit Trails:** Strict, immutable audit logs that track exactly who, when, and how any change is made to a student's grades.

7. Fee & Financial Management

A robust financial engine for complete visibility into the school's revenue streams.

- **Fee Structures:** Configurable fee categories (e.g., tuition, transport, library) mapped to specific classes or student types.
- **Payment Tracking:** Real-time logging of fee collections and outstanding balances.
- **Automated Alerts:** System-generated reminders and pending-due alerts sent to parents.
- **Financial Reporting:** Detailed financial breakdowns, collection summaries, and outstanding reports.

8. Communication (SMS) Module

A direct line of communication to close the gap between the school and parents.

- **Approved Templates:** Standardized, pre-approved custom SMS templates for consistent messaging.
- **Targeted Messaging:** Bulk SMS dispatch to saved recipient lists (e.g., specific classes, defaulters, all staff).
- **Automation & Scheduling:** Scheduled messaging for upcoming events and automated birthday greetings.
- **Delivery Tracking:** Full delivery logs indicating the success, failure, and status of all sent messages.

9. Bulk Operations & Data Migration

Efficiency tools designed to reduce hours of manual administrative work down to a few clicks.


- **Data Ingestion:** Seamless import integrations supporting CSV, Excel, and Google Sheets for rapid onboarding.
- **Data Export:** Quick extraction of systemic data for external backups or analysis.
- **Mass Updates:** Guided workflows for bulk data edits (e.g., updating fee structures for a whole class).
- **High-Volume Tasks:** Streamlined handling of bulk student transfers, promotions, and status changes.

10. Admin Dashboard & Custom Reporting

The real-time command center and intelligence hub for school leadership.

- **Executive Dashboard:** At-a-glance KPIs including daily attendance trends, SMS delivery statuses, staff workloads, and upcoming birthdays.
- **Dynamic Customization:** Admin-level controls to add new configurable fields and validation rules to forms without requiring developer intervention.
- **Dynamic Report Builder:** Generate precise, tailored reports without manual data compilation.
- **One-Click Export:** Instantly export generated reports to PDF or Excel formats for distribution.

6. Technical Approach

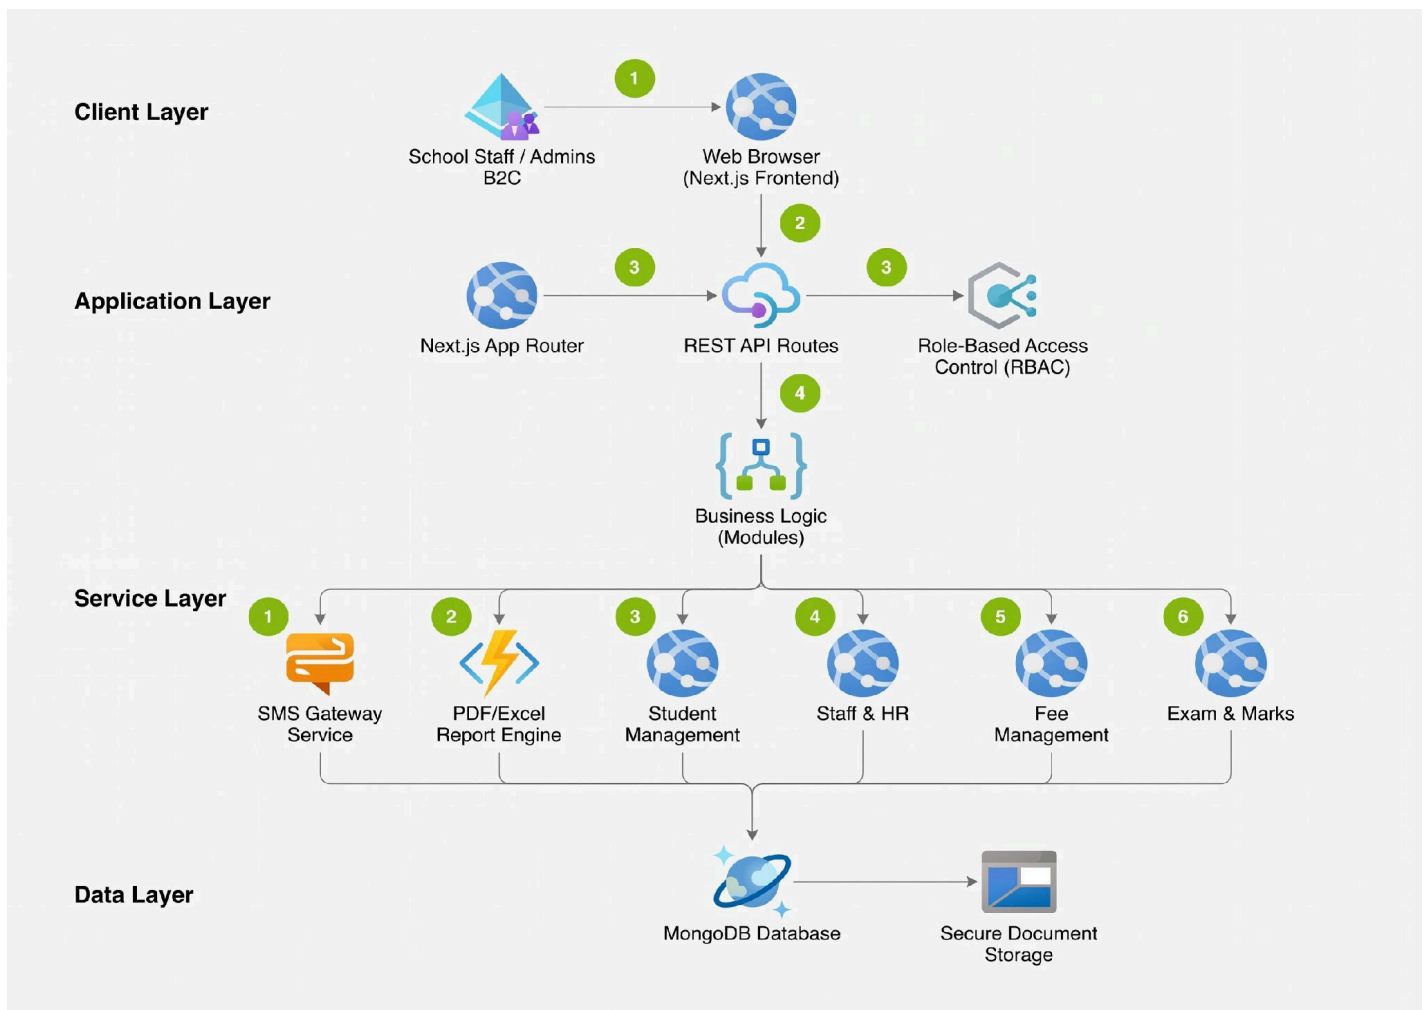

Frontend & Backend Framework — Next.js

Next.js has been chosen to power both the admin and school-facing interfaces, giving the platform a fast, unified, and highly maintainable full-stack architecture.

Database — MongoDB

A flexible, scalable NoSQL database well suited to the varied and evolving nature of school records — students, staff, academics and fees — without rigid schema constraints.

Access Control — Role-Based Access (RBAC)

Super Admin, administrative staff, teaching staff, and other user roles are each granted access strictly scoped to their function, protecting sensitive student, staff and financial data from unauthorised access.

Infrastructure — Dedicated VPS Hosting

The system will be deployed on dedicated Virtual Private Server (VPS) infrastructure, scaled for the target base of 20 Users, on an expandable architecture that supports future growth without requiring a platform rebuild.

5. Key Benefits & Value Proposition

- Complete transparency — every stakeholder works from the same real-time data, eliminating discrepancies between departments.
- Stronger parent engagement — automated, reliable SMS communication directly closes the existing gap between school and home.
- Faster, better-informed decisions — live dashboards and KPIs give leadership exactly what they need, when they need it.
- Reduced administrative burden — bulk operations and automation cut down significantly on repetitive manual work.
- Built to grow — architecture scoped and load-tested for 2,500 users from day one, with room to expand.
- Secure by design — role-based access ensures every user sees only the data relevant to their role.

7. Implementation Timeline & Milestones

The standard estimated delivery window for this project is 4–6 weeks from project commencement to full deployment. The exact schedule will be mutually confirmed upon signing.

PHASE	DURATION	KEY DELIVERABLES
Phase 1 — Discovery & Planning	Week 1	Requirement finalisation, architecture & database design, environment and VPS setup
Phase 2 — Core Module Development	Week 2 – 3	Student Management, Staff & HR Management, Fee Management (25% milestone payment due on completion)
Phase 3 — Extended Module Development	Week 3 – 5	Marks & Examination, Administrative Dashboard, Communication (SMS), Custom Reporting, Bulk Operations, Dynamic Customisation, Data Import/Export, Academic Year Management
Phase 4 — Testing, Deployment & Handover	Week 5 – 6	QA & UAT, data migration, final deployment, training and handover (final 25% milestone payment due)

8. Investment & Commercial Proposal

Investment Area	Description	Cost (INR)
Development Budget (Phase 1)	One-time fee for full-stack system development, testing, and initial deployment.	₹34,999
Operational Cost (Year 1)	Dedicated VPS hosting (12 months), scaled for 2,500 target users, on expandable architecture.	₹7,500
Total Year 1 Investment	Total capital required to launch and run the system for the first year.	₹42,499
Recurring Annual Cost	Infrastructure renewal from Year 2 onward (subject to change based on user expansion).	₹7500/ yr

9. Payment Schedule

- 50% advance payment upon signing of this proposal, to initiate Phase 1.
- 25% upon completion of the core modules — Student Management, Staff Management, and Fee Management.
- 25% upon final deployment and handover of the completed system.

10. Post-Launch Support & Maintenance

Monsrow's commitment to Venus School does not end at deployment. This engagement includes:

- 30 days of complimentary support immediately following deployment, covering the resolution of any bugs or issues arising from day-to-day use.
- One year of continued technical support beyond the complimentary period, to help ensure the system remains stable and reliable as usage and data volumes grow. Specific terms of this continued support will be mutually confirmed at handover.

11. Terms & Conditions

SMS Gateway

SMS credits are not included in the development or VPS budget outlined in this proposal. Venus School will purchase SMS credits directly from the integrated gateway provider as needed.

Timeline

The project delivery timeline is to be mutually agreed upon signing. The standard estimate is 4–6 weeks from project commencement to full deployment.

Proposal Validity

This proposal is valid for 10 days from its date of issue, i.e. until August 4, 2026. Pricing and timelines beyond this date are subject to review.

Ownership & Intellectual Property

Full ownership of the developed system and its source code transfers to Venus School upon receipt of the final and full payment outlined in the Payment Schedule.

12. Assumptions & Exclusions

- Venus School will provide all existing student and staff data required for migration, in a usable digital format (e.g. Excel or CSV).
- Domain name registration and any associated renewal costs are the responsibility of Venus School.
- SMS gateway credits are excluded from this proposal and will be purchased directly by Venus School (see Terms & Conditions).
- Any modules, features, or integrations not explicitly listed in the Scope of Work (Section 4) are considered out of scope and will be quoted separately upon request.

13. Why Partner With Team Monsrow

Monsrow is a team of dedicated developers who have delivered 25+ real-world software projects across a range of industries. We take a hands-on, practical approach to engineering — building systems that solve genuine operational problems rather than adding unnecessary complexity.

From planning through deployment, our team stays directly involved at every stage of the project, giving Venus School a single, accountable point of contact throughout the engagement.

14. Next Steps

- Review this proposal and share any questions or requested adjustments.
- Confirm acceptance by signing and returning this document.
- Submit the 50% advance payment to initiate Phase 1.
- Monsrow schedules a kickoff call to confirm the final project timeline and begin development.

15. Contact & Signature Block

We look forward to partnering with Venus School on this project. For any questions regarding this proposal, please reach out to Rajakumaran P at Team Monsrow.

For Team Monsrow

Signature

Rajakumaran P
Team Monsrow

Date: _____

For Venus School

Signature

Name: _____

Designation: _____

Date: _____
